

Project: Van Phong Bonded Petroleum Terminal
 Location: My Giang Island - Ninh Hoa District
 Contractor: Song Hong Construction JSC (INCOMEX)
 Package 02: Civil & Building in Van Phong Terminal


Reported date: **14-Apr-10**
 Revision No.: 0

- Foreign currency: USD 8,357,940.29

8.6 MONTHLY PROGRESS TABLE & "S" CURVE (BẢNG TIẾN ĐỘ VÀ BIỂU ĐỒ CHỮ S)

	Year	2008												2009						2010									
		Project Mth No	1	2	3	4	5	6	7	8	9	10	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	
		Calendar Mth	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC	JULY	AUG	SEP	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT
Construction	Plan Cumulative		0.00%	1.31%	2.39%	4.29%	6.26%	8.44%	10.58%	12.73%	14.88%	17.03%	17.51%	17.99%	18.47%	18.95%	19.43%	24.24%	29.24%	34.24%	43.63%	54.60%	65.40%	74.36%	82.03%	89.37%	95.33%	100.00%	
	Plan Monthly		0.00%	1.31%	1.08%	1.90%	1.97%	2.18%	2.14%	2.15%	2.15%	2.15%	0.48%	0.48%	0.48%	0.48%	0.48%	4.81%	5.00%	5.00%	9.39%	10.97%	10.80%	8.96%	7.67%	7.34%	5.96%	4.67%	
	Actual Monthly			1.31%	1.08%	1.90%	1.90%	2.18%	2.15%	2.15%	2.15%	2.15%	0.48%	0.48%	0.48%	0.48%	0.48%	4.81%	3.34%	3.34%									
Wt % = 1.31%	Actual Cumulative		0.00%	1.31%	2.39%	4.29%	6.26%	8.43%	10.58%	12.73%	14.88%	17.03%	17.51%	17.99%	18.47%	18.95%	19.43%	24.24%	27.57%	30.91%									

PROGRESS S-CURVE FOR CIVIL AND BUILDING CONSTRUCTION WORK

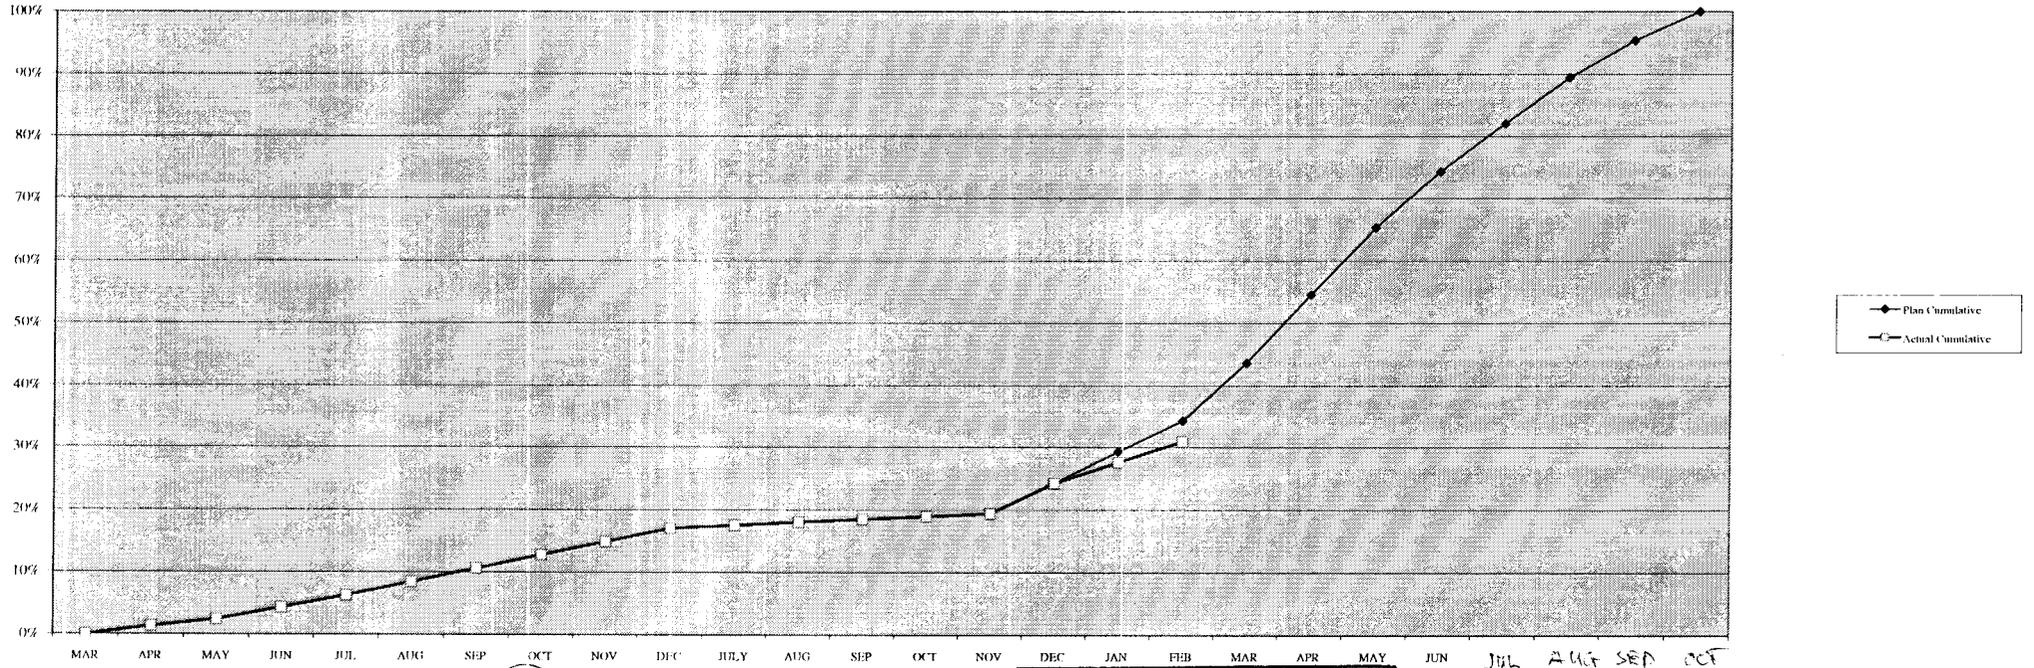

SUBMITTED BY,

VU NGOC KHANH
QA / QC

D, PROJECT MANAGER

LUONG VIET DUNG

CT CP XÂY DỰNG SÔNG HỒNG
 CÔNG TY CP XÂY LẬP INCOMEX

BAN QUẢN LÝ DỰ ÁN
KHO XĂNG DẦU
NGOẠI QUẬN VÂN PHONG

ĐT: 058.3622704 FAX: 058.3622703
